

## Agenda Item #10 - Construction Amendments and Changes Log (Transit Center)

5/24/2019

Trade Package	CCO/CR No.	Total Value	Date submitted to CRC	Date No Exceptions Taken by CRC	Amount No Exceptions Taken by CRC	CCO Final Approved Amount	CCO Category	Contingency Source	Fund Source	CCO Issue
<b>Code Compliance</b>										
10.4	COR 311826	\$ 650,000	2/16/2018	2/16/2018	\$ 650,000		Code Compliance	TJPA	CFD	Fire Management System Changes
<b>Coordination</b>										
7.2/7.6	COR 311374	\$ 375,000	8/31/2017	8/31/2017	\$ 375,000		Coordination	CMGC	CFD	Curb Extension at Elevator Fronts for All Elevator Shafts
10.2	COR 311901	\$ 700,000	2/16/2018	2/16/2018	\$ 700,000		Coordination	CMGC	CFD	RFI T-6025 - Revised Supports to Account for Phase 2 Mechanical Duct
<b>Errors &amp; Omissions</b>										
7.2	COR	\$ 3,000,000	11/10/2017	11/17/2017	\$ 3,000,000		Errors & Omissions	TJPA	CFD	General Closeout Items
7.2	COR	\$ 310,000	8/31/2017	8/31/2017	\$ 310,000		Errors & Omissions	TJPA	CFD	Escalator Issues - Added Mid-Span Support.
10.2	COR 311901	\$ 1,000,000	8/24/2018	8/24/2018	\$ 1,000,000		Errors & Omissions	TJPA	CFD	Revised Supports for Piping in Service Corridors
10.4	COR	\$ 300,000	8/24/2018	8/24/2018	\$ 300,000		Errors & Omissions	TJPA	CFD	RFI T-6974.1 Modified LE-281 Fixture and Power Feed Location
10.4	COR	\$ 300,000	8/24/2018	8/24/2018	\$ 300,000		Errors & Omissions	TJPA	CFD	RFI-T 6854.1 Installation of Dedicated Emergency Circuit for Elevator Monitoring System
10.4	COR 313473	\$ 2,000,000	8/24/2018	8/24/2018	\$ 2,000,000		Errors & Omissions	TJPA	CFD	RFI T-7267 Power to Signage Pylons
10.4	COR 312021	\$ 800,000	2/16/2018	2/16/2018	\$ 800,000		Errors & Omissions	TJPA	CFD	RFI T-5960 Added Door Power
10.4	COR 312719	\$ 350,000	2/16/2018	2/16/2018	\$ 350,000		Errors & Omissions	TJPA	CFD	IDF Room Build-out
10.4	COR 311105	\$ 2,300,000	11/7/2016	11/18/2016	\$ 2,300,000		Errors & Omissions	TJPA/CMGC	CFD	Hardened Conduit RFI T-3669
13.1	COR 311562	\$ 100,000	8/31/2017	8/31/2017	\$ 100,000		Errors & Omissions	TJPA	CFD	Change to Glass Type for Bus Glass Wall
16.0	COR	\$ 1,000,000	2/16/2018	2/16/2018	\$ 1,000,000		Errors & Omissions	TJPA/CMGC	CFD	Skanska General Scope Closeout Items
18.1	COR 310480	\$ 700,000	11/10/2017	11/17/2017	\$ 700,000		Errors & Omissions	TJPA	TIFIA	Revised sizes for Link Beams per ASI 150, General Design Issues
18.1	COR	\$ 1,000,000	11/10/2017	11/17/2017	\$ 1,000,000		Errors & Omissions	TJPA	CFD	General Closeout Items
7.2	COR 311408	\$ 3,300,000	5/8/2017	5/19/2017	\$ 3,300,000	\$ 2,045,732	Errors & Omissions	TJPA	CFD	W-Systems Impact to Structural Concrete Package. COR submitted at \$6.3M, but \$3M due to inefficiencies /delays
7.2	COR 311981	\$ 900,000	8/31/2017	8/31/2017	\$ 900,000	\$ 783,827	Errors & Omissions	TJPA	CFD	Rebar Changes from Bid Including ASI 128
7.2	CCO 0426	\$ 1,000,000	2/6/2017	2/17/2017	\$ 1,000,000	\$ 443,801	Errors & Omissions	TJPA	TIFIA	Built Up Slabs in Ground Level and Roof Level
7.3	CCO 0412	\$ 97,000	8/31/2017	8/31/2017	\$ 97,000	\$ 76,576	Errors & Omissions	TJPA	City Financing	Roof Park Restaurant Cable Guardrail Continuity Plate per RFI T-5041 Series
8.11R	CCO 0416	\$ 912,000	5/8/2017	5/19/2017	\$ 912,000	\$ 859,088	Errors & Omissions	TJPA	TIFIA	W-13 Frame Modifications
8.11R	CCO 1063	\$ 270,000	5/8/2017	5/19/2017	\$ 270,000	\$ 254,915	Errors & Omissions	TJPA	TIFIA	W-12 Perimeter Expansion Joint Infill Plate
8.4	311044	\$ 300,000	11/10/2017	11/17/2017	\$ 300,000	\$ 290,121	Errors & Omissions	TJPA	CFD	ASI 141 Changes for Metal Panel System
10.2	COR 311542	\$ 1,010,000	11/10/2017	11/17/2017	\$ 1,010,000	\$ 917,040	Errors & Omissions	TJPA	CFD	Gray Water System Clarification RFIs
10.2	COR 311439	\$ 500,000	5/8/2017	5/19/2017	\$ 500,000	\$ 487,824	Errors & Omissions	TJPA	CFD	DBI Venting Requirements - CCO 0390, 594,0561
10.2	CCO 0402	\$ 660,000	8/31/2017	8/31/2017	\$ 660,000	\$ 617,304	Errors & Omissions	TJPA	TIFIA	ASI 138 Revisions
10.2	CCO 0343	\$ 800,000	2/6/2017	3/22/2017	\$ 800,000	\$ 673,785	Errors & Omissions	TJPA	TIFIA	Connection to Sewer Mains per RFI T-5029
10.2	COR 312336	\$ 450,000	11/10/2017	11/17/2017	\$ 450,000	\$ 345,012	Errors & Omissions	TJPA	CFD	RFI T-6805 Wrapping Fuel Oil Piping in Lieu of 2 Hour Enclosure
10.4	COR 311110	\$ 325,000	8/31/2017	8/31/2017	\$ 325,000	\$ 323,964	Errors & Omissions	TJPA	CFD	TG10.4 ASI 141 Electrical Changes
13.1	COR 311561	\$ 350,000	8/31/2017	8/31/2017	\$ 350,000	\$ 134,590	Errors & Omissions	TJPA	CFD	Shoe Design Changes at Bus Fountain
13.2	CCO 0362	\$ 300,000	5/8/2017	5/19/2017	\$ 300,000	\$ 297,101	Errors & Omissions	TJPA	City Financing	Add FC 4 Layers and revision to INS-14 per ASI 138
18.1	COR 312068	\$ 300,000	11/10/2017	11/17/2017	\$ 300,000	\$ 233,583	Errors & Omissions	TJPA	TIFIA	Changes to Cal Trans Substation Building Lot Elevations
18.1	COR 311099	\$ 1,500,000	11/10/2017	11/17/2017	\$ 1,500,000	\$ 367,498	Errors & Omissions	TJPA	City Financing	Hinge 9 Expansion Joint
18.1	CCO 0290.1	\$ 736,000	8/22/2016	8/24/2016	\$ 736,000	\$ 691,702	Errors & Omissions	TJPA	Bridge Loan	Revisions to the Bus Ramp Cable Stay Hinge 8 Expansion Joint per ASI 150-015.
18.1	CCO 0373.1	\$ 475,000	8/22/2016	8/24/2016	\$ 475,000	\$ 367,498	Errors & Omissions	TJPA	TIFIA	Revisions to the Bus Ramp Cable Stay Hinge 9 Expansion Joint per ASI 150-016.
<b>Owner Requested</b>										
7.2	*COR 310937	\$ 800,000	8/31/2017	8/31/2017	\$ 800,000	\$ 647,117	Owner Requested	TJPA	TIFIA	Pour backs for curbs, other curb issues related to W2 system, General Closeout Items (CCO 0610)
7.2	CCO 0324	\$ 455,000	2/6/2017	2/17/2017	\$ 455,000	\$ 428,811	Owner Requested	TJPA	City Financing	Gantry Beams at Ground Level above Transformer Vaults per ASI 121
7.2	CCO 0312	\$ 750,000	11/7/2016	11/18/2016	\$ 750,000	\$ 708,975	Owner Requested	TJPA	TIFIA	Additional Wall Plates at Lower Concourse Walls
7.2	CCO 0269.1	\$ 325,000	8/22/2016	8/24/2016	\$ 325,000	\$ 254,308	Owner Requested	TJPA	Land Sales	Added plate to short curbs to support deformed bars per RFI T-3184 and added plates for tall curbs between GL 10-20
7.2	CCO 0291	\$ 368,000	8/22/2016	8/24/2016	\$ 368,000	\$ 317,592	Owner Requested	TJPA	Land Sales	Install additional rebar, formwork and concrete for Partition walls at Lower Concourse per ASI 128.
7.6	COR 311367	\$ 260,000	11/7/2016	11/18/2016	\$ 260,000	\$ (101,621)	Owner Requested	TJPA	CFD	Changes to the GL 35 Seismic Joints due to the OCS footing interrupting the joints and replacing the SJ cover with 1" steel plate
7.6	CCO 0316	\$ 694,000	8/22/2016	8/24/2016	\$ 694,000	\$ 546,055	Owner Requested	TJPA/Reimbursable	Salesforce Tower	Added seismic joint at Salesforce Tower Pedestrian Bridge per ASI 137
10.2	COR 310461.2	\$ 325,000	5/18/2018	5/18/2018	\$ 325,000	\$ 289,110	Owner Requested	TJPA	CFD	CM/GC Trailer Relocation Due to TJPA Sale of Lot N (CCO 0588)
10.3	CCO 0304	\$ 118,000	2/6/2017	2/17/2017	\$ 118,000	\$ 117,841	Owner Requested	TJPA	City Financing	Roof Park scope, Heat Pump Changes, & Duct Reroute per ASI 128
10.4	COR 310744	\$ 7,400,000	2/16/2018	2/16/2018	\$ 7,400,000	\$ 1,494,638	Owner Requested	TJPA	CFD	ASI 131 "No Fly Zone" (CCO 0622)
13.1	CCO 0366	\$ 420,000	2/6/2017	2/17/2017	\$ 420,000	\$ 7,185	Owner Requested	TJPA	City Financing	Landscape Changes per ASI 138
<b>Schedule Mitigation</b>										

# Agenda Item #10 - Construction Amendments and Changes Log (Transit Center)

5/24/2019

Trade Package	CCO/CR No.	Total Value	Date submitted to CRC	Date No Exceptions Taken by CRC	Amount No Exceptions Taken by CRC	CCO Final Approved Amount	CCO Category	Contingency Source	Fund Source	CCO Issue
7.2	COR 311070.1	\$ 450,000	2/16/2018	2/16/2018	\$ 450,000		Schedule Mitigation	CMGC	CFD	Dry Finish Acceleration Part 2
8.6R	COR 312232	\$ 800,000	2/16/2018	2/16/2018	\$ 800,000		Schedule Mitigation	CMGC	CFD	Storage of W-14 Ceiling Panels
10.4	COR 311616.2	\$ 280,000	2/16/2018	2/16/2018	\$ 280,000		Schedule Mitigation	CMGC	CFD	Single Line - Acceleration
10.4	COR 311967	\$ 380,000	2/16/2018	2/16/2018	\$ 380,000		Schedule Mitigation	CMGC	CFD	Electrical Zone 4 Acceleration
10.4	COR	\$ 600,000	2/16/2018	2/16/2018	\$ 600,000		Schedule Mitigation	CMGC	CFD	Supplemental Man-power - Rosendin
10.4	COR 311736	\$ 310,000	2/16/2018	2/16/2018	\$ 310,000		Schedule Mitigation	CMGC	CFD	SFPUC Vault Acceleration
16.0	COR 311825	\$ 600,000	11/10/2017	11/17/2017	\$ 600,000		Schedule Mitigation	TJPA	CFD	Skanska Inefficiency Costs
5.10	COR 312195.1	\$ 280,000	2/16/2017	2/16/2017	\$ 280,000	\$ 259,546	Schedule Mitigation	CMGC	CFD	Grand Hall Temporary Floor Protection
7.2	CCO 1059	\$ 1,200,000	2/6/2017	2/17/2017	\$ 1,200,000	\$ 895,298	Schedule Mitigation	CMGC	TIFIA	Schedule Recovery for TG 7.2 scope, premium time only, using CM/GC Contingency per contract.
7.6	COR	\$ 1,000,000	2/16/2018	2/16/2018	\$ 1,000,000	\$ 951,440	Schedule Mitigation	CMGC	CFD	Trade Package 12.1 to 07.6 Scope Transfer Reconciliation (Ref CCO 503, 1112, and Zones 1-3)
<b>Scope Procurement</b>										
7.2	COR 310599	\$ 650,000	11/10/2017	11/17/2017	\$ 650,000.00		Scope Procurement	CMGC	CFD	Deck Steel Plates at Tall Curbs
7.2	COR 311646	\$ 370,000	11/10/2017	11/17/2017	\$ 370,000.00		Scope Procurement	CMGC	CFD	Roof Built Up Slab
10.2	COR 311837.1	\$ 700,000	8/24/2018	8/24/2018	\$ 700,000.00		Scope Procurement	TJPA	CFD	PG&E added Supports for Gas Meter
10.4	COR 312021.2	\$ 450,000	8/24/2018	8/24/2018	\$ 450,000.00		Scope Procurement	TJPA	CFD	120V Power to Crown Corr Doors
10.4	COR 311397	\$ 2,100,000	2/16/2018	2/16/2018	\$ 2,100,000.00		Scope Procurement	CMGC	CFD	A1 Light Fixtures
10.4	CR T-517	\$ 2,500,000	11/10/2017	11/17/2017	\$ 2,500,000.00		Scope Procurement	TJPA	CFD	TG10.4 Revised ERRCS Scope From ASI 134
14.1B	COR 311970	\$ 450,000	8/31/2017	8/31/2017	\$ 450,000		Scope Procurement	TJPA	CFD	Addition of LED Skirt Lighting, Increased Foot Candela and Other Emergency Backup Elements
n/a	CCO 0410	\$ 42,000	8/31/2017	8/31/2017	\$ 42,000	\$ 41,689	Scope Procurement	TJPA	City Financing	Roof Park Restaurant Handrail IPE Wood Cap
	COR	\$ 43,600	11/10/2017	11/17/2017	\$ 43,600	\$ 43,600	Scope Procurement	TJPA	CFD	Tim Hawkinson Concrete Removal Contract
4.2	CR T-383.A	\$ 5,500,000	4/5/2018	4/5/2018	\$ 5,500,000	\$ 1,563,188	Scope Procurement	TJPA	CFD	Traction Power (Base Scope up to 2nd Street). \$5.5 million was presented to the CRC on 2/16/18.
4.2	CR T-383.A	\$ 4,500,000	4/5/2018	-	n/a		Scope Procurement	TJPA	n/a	Traction Power (2nd Street to 5th Street) - Scope Voided
4.2	COR 311395	\$ 550,000	11/10/2017	11/17/2017	\$ 550,000	\$ 258,750	Scope Procurement	TJPA	CFD	OCS Fiberglass Support System Installation
5.XX	CCO 1129, 1132	\$ 4,500,000	2/16/2018	2/16/2018	\$ 4,500,000	\$ 4,500,000	Scope Procurement	CMGC	CFD	Additional Temporary Facilities for Phased Completion (Post December 22, 2017)
5.10	CCO1137	\$ 3,350,000	4/5/2018	3/21/2018	\$ 3,350,000	\$ 3,350,000	Scope Procurement	CMGC	CFD	Additional Temporary Facilities for Phased Completion, for June through August 2018
5.10	COR 310496	\$ 1,400,000	11/10/2017	11/17/2017	\$ 1,400,000	\$ 1,398,300	Scope Procurement	TJPA	CFD	Overhead Protection at First and Fremont
5.10	COR 310505.1	\$ 1,108,000	11/10/2017	11/17/2017	\$ 1,108,000	\$ 1,052,716	Scope Procurement	TJPA	CFD	Site Dewatering
5.10	COR 310841.1	\$ 2,170,000	11/10/2017	11/17/2017	\$ 2,170,000	\$ 1,780,013	Scope Procurement	TJPA	CFD	Furnish Site Dumpsters for LEED Related Construction Waste
5.10	COR 312079	\$ 500,000	11/10/2017	11/17/2017	\$ 500,000	\$ 477,112	Scope Procurement	TJPA	CFD	Provide Plywood Backer Boards for IDF/MDF Rooms
7.2	CCO 0393.1	\$ 250,000	2/6/2017	2/17/2017	\$ 250,000	\$ 87,153	Scope Procurement	TJPA	MTC AB1171	Drum Café Revisions
7.2	CCO 0328	\$ 445,000	11/7/2016	11/18/2016	\$ 445,000	\$ 434,946	Scope Procurement	TJPA	City Financing	West Throat Vent Shaft Concrete
7.3	CCO 0370	\$ 60,000	5/8/2017	5/19/2017	\$ 60,000	\$ 56,579	Scope Procurement	TJPA	City Financing	Bent Plate Embed and SS Base Plate from ASI 128 for Roof Park Restaurant
7.6	CCO 1035	\$ 330,000	8/22/2016	8/24/2016	\$ 330,000	\$ 307,144	Scope Procurement	CMGC	Land Sales	Installation of Mat Slab walls at water storage tank previously not procured.
8.4	COR 310812	\$ 450,000	2/16/2018	2/16/2018	\$ 450,000	\$ 416,919	Scope Procurement	CMGC	CFD	W-1 and W16C Installation Buy-out Design Impacts
8.6R	CCO 0344	\$ 480,000	5/8/2017	5/19/2017	\$ 480,000	\$ 476,903	Scope Procurement	TJPA	TIFIA	ASI 140 Drop-in Span Aluminum Enclosure, VE Item.
8.6R	CCO 0309	\$ 250,000	2/6/2017	2/17/2017	\$ 250,000	\$ 249,554	Scope Procurement	TJPA	City Financing	Procurement of the W2 and W3 head of wall assembly
8.11R	CCO 0378	\$ 480,000	8/31/2017	8/31/2017	\$ 480,000	\$ 475,387	Scope Procurement	TJPA	TIFIA	Procurement of Glazing Door Hardware Package previously not procured. **Estimate increased
10.2	CCO 0186	\$ 1,486,000	8/22/2016	8/24/2016	\$ 1,486,000	\$ 1,232,298	Scope Procurement	TJPA	Prop K	Revisions and additions to plumbing system per ASI 128.
10.4	COR 312695	\$ 595,000	4/5/2018	3/21/2018	\$ 595,000	\$ 593,007	Scope Procurement	TJPA	CFD	E2 Pylon Louvers and Frosted Lens
10.4	COR 311671.1	\$ 600,000	8/31/2017	8/31/2017	\$ 600,000	\$ 463,487	Scope Procurement	TJPA	CFD	E2 Pylon Beacon Power per RFI T-4988
10.4	CCO 0284	\$ 1,330,000	11/7/2016	11/18/2016	\$ 1,330,000	\$ 1,202,996	Scope Procurement	TJPA	TIFIA	Phase 1.5 ASI 144
10.4	CCO 0293.1	\$ 1,100,000	8/22/2016	8/24/2016	\$ 1,100,000	\$ 861,630	Scope Procurement	TJPA	TIFIA	Procurement of the pathway that supports the Emergency Response System per ASI 134.
10.4	CCO 0379	\$ 390,000	3/22/2017	3/22/2017	\$ 390,000	\$ 275,056	Scope Procurement	TJPA	TIFIA	Added Stairwell Lighting per RFI T-5585.1
10.4	COR 311155-1	\$ 1,200,000	4/5/2018	3/21/2018	\$ 1,200,000	\$ 998,337	Scope Procurement	TJPA	CFD	ASI 143 - Incorporation of Phase 1.5 Converge Network Package (CCO 0540 & 0643)
10.4	*COR 311034	\$ 1,100,000	8/31/2017	11/17/2017	\$ 1,100,000.00	\$ 228,691	Scope Procurement	TJPA/Reimbursable	SFPUC	SFPUC Switchgear and Cabling Additional Work. (CCO 0652)
12.1	COR	\$ 1,500,000	2/16/2018	2/16/2018	\$ 1,500,000	\$ 1,320,803	Scope Procurement	TJPA	CFD	Traffic Signal Revisions and Streetlight Revisions (Ref CR T-502, T-571, and T-543)
13.1	COR 311740	\$ 300,000	8/31/2017	8/31/2017	\$ 300,000	\$ 97,298	Scope Procurement	TJPA	City Financing	Contract Grow Monthly Maintenance and Storage
13.2	CCO 0277	\$ 435,000	8/22/2016	8/24/2016	\$ 435,000	\$ 401,828	Scope Procurement	TJPA	Land Sales	Procurement and installation of the W2 Roof Trellis and Outriggers per ASI 128 and 138
16.0	COR 312686	\$ 450,000	2/16/2018	2/16/2018	\$ 450,000	\$ 198,633	Scope Procurement	TJPA	CFD	CR T-319 ASI 148 Incorporation of RFI Responses (CCO 0583)
16.8	CCO 0287	\$ 261,000	8/22/2016	8/24/2016	\$ 261,000	\$ 252,310	Scope Procurement	TJPA	Land Sales	Installation of the Rooftop Restaurant Fireproofing per ASI 128
<b>Closeout/Settlement</b>										
Various	*COR	\$ 17,414,000	8/24/2018	8/24/2018	\$ 17,414,000	\$ 3,970,313	Various			General Closeout Items for all Trades and Resolution of Resolvable Claims. As of January 2019, \$3.4M of the
7.1	CCO 1043	\$ 425,000	2/6/2017	2/17/2017	\$ 425,000	\$ 425,742	Skanska Settlement	CMGC	TIFIA	Seismic Upgrades to Access Trestle. ** Final amount \$742 over NTE of \$425,000.
7.1	COR 310296.1	\$ 672,750	8/22/2016	8/24/2016	\$ 672,750	\$ 637,974	BBII Settlement	TJPA	CFD	Removal of Sand Inclusions in Bus Deck level cast node pads, CCO 428 added
<b>Total</b>										
		<b>\$109,772,350</b>					<b>CCO Final Approved Total</b>	<b>\$47,157,610</b>		

## Agenda Item #10 - Construction Amendments and Changes Log (Transit Center)

5/24/2019

Trade Package	CCO/CR No.	Total Value	Date submitted to CRC	Date No Exceptions Taken by CRC	Amount No Exceptions Taken by CRC	CCO Final Approved Amount	CCO Category	Contingency Source	Fund Source	CCO Issue
---------------	------------	-------------	-----------------------	---------------------------------	-----------------------------------	---------------------------	--------------	--------------------	-------------	-----------

\* Executed since last CRC meeting

\*\* Increased Total Value from Previously Approved

MODS and amounts paid directly by WOJV (not thru TJPA) are not included in this estimate

New Construction Changes

In Process (Presented to CRC)

Approved

**Trade Packages:**

4.2	Utility Relocation - Mission St. AWSS		10.3	Mechanical/HVAC
5.1	Temporary Facilities		10.4	Electrical
7.1	Structural Steel		10.5	Fire Protection and Suppression
7.2	Structural Concrete		12.1	Civil/Site Work at Grade/Ground Level Landscaping
7.3	Miscellaneous Metal		13.1	Landscaping and Irrigation
7.6	Topping Slabs, Bus Crash Rail and Expansion Joints		13.2	Roofing/Waterproofing
8.4	Metal Panels		14.1B	Escalators
8.6R	Metal Ceilings		16.0	Interiors/Finishes
8.11R	Glass Curtain Wall/Skylights		16.8	Fireproofing/Intumescent Spray
10.2	Plumbing		18.1	Bus Ramp

















### Modifications and Construction Change Orders as of May 2019 (In Millions)

A	B	C	D	E	F	G	H	I
<b>*Contract Sum to date (in Millions) (B+C+I)</b>	<b>Base Scope WOJV</b>	<b>Scope Procurement</b>	<b>Code Issues</b>	<b>Errors &amp; Omissions</b>	<b>**Owner Requested Change</b>	<b>Unforeseen Conditions</b>	<b>***CMGC Contingency</b>	<b>Total of Non-Base Scope Costs (D+E+F+G+H)</b>
\$1,429.3	\$1,220.5	\$113.0	\$3.8	\$21.0	\$10.8	\$22.9	\$37.3	\$95.8
	85.39%	7.91%	0.27%	1.47%	0.76%	1.60%	2.61%	6.70%

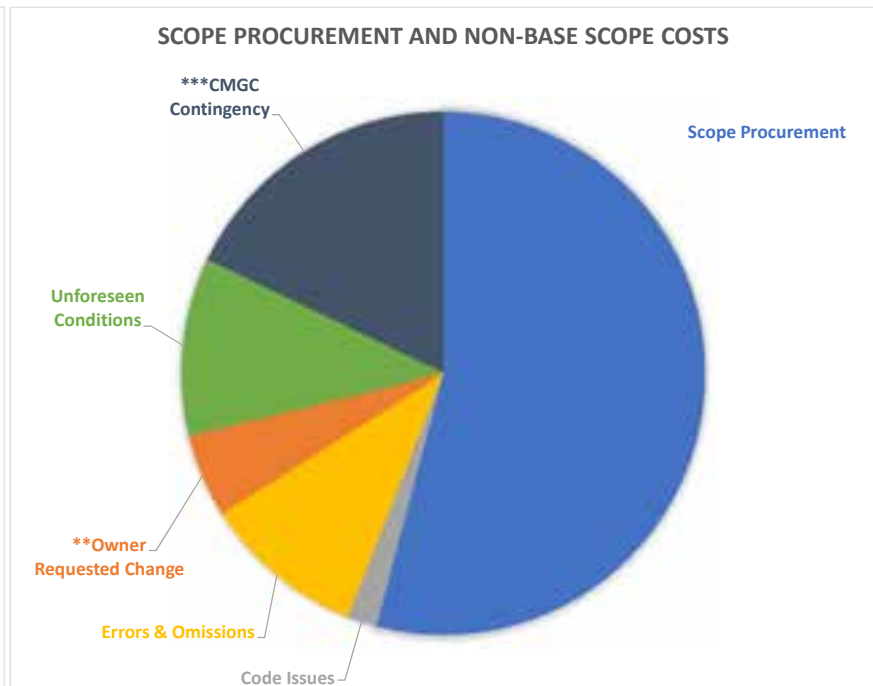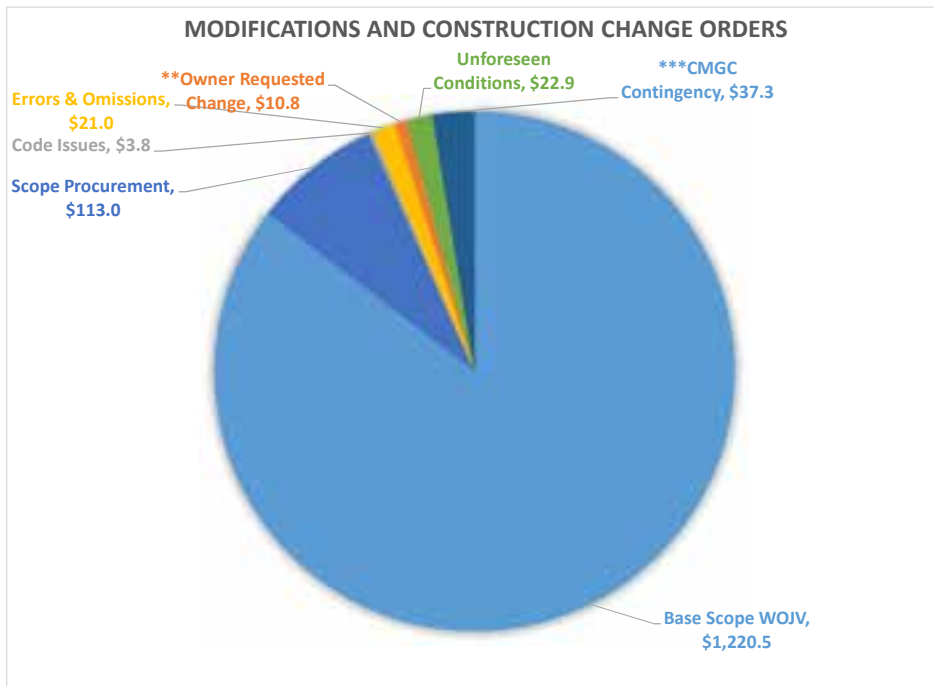

- \* Contract Sum includes Preconstruction, Geotechnical Engineering, and Fees but does not include General Contractor Reimbursable Expenses
- \*\* Includes Third Party Reimbursable CCOs and Owner Directed Schedule Mitigation
- \*\*\* Includes Coordination Issues, Settlement Items, and Schedule Mitigation

Executed CCOs as of 5/24/19
